



1250 West Century Avenue
Mailing Address:
P.O. Box 5601
Bismarck, ND 58506-5601
(701) 530-1600

July 22, 2021

Kimberly D. Bose, Secretary
Federal Energy Regulatory Commission
888 First Street, N.E., Room 1A
Washington, D.C. 20426

Re: WBI Energy Transmission, Inc.
Docket Nos. CP20-52-000 and CP20-52-001
North Bakken Expansion Project
Weekly Status Report No. 7

Dear Ms. Bose:

WBI Energy Transmission, Inc. (WBI Energy) herewith submits its Weekly Status Report No. 7 for the North Bakken Expansion Project, in compliance with Environmental Condition 8 of the Appendix to the Federal Energy Regulatory Commission's June 1, 2021 Order Issuing Certificate in the above referenced dockets.

The attached report addresses the period July 12, 2021 to July 18, 2021.

Should you have any questions or comments regarding this filing, please call the undersigned at (701) 530-1563.

Sincerely,

/s/ Lori Myerchin

Lori Myerchin
Director, Regulatory Affairs and
Transportation Services

Courtesy Copies:

Dawn Ramsey, FERC
Shannon Crosley, FERC



WBI Energy Transmission, Inc.
North Bakken Expansion Project Status Report No. 7
FERC Docket Nos. CP20-52-000
CP20-52-001

Reporting Period: July 12, 2021 through July 18, 2021

A. Update on Federal Authorizations

WBI Energy has obtained all necessary federal permits and authorizations required for construction of the North Bakken Expansion Project.

B. Construction Status - Pipeline Facilities

- Migratory bird nesting surveys began on July 13, 2021 and are ongoing on the pipeline right-of-way.
- WBI Energy held a second virtual environmental training for construction of the Project on July 15, 2021. Environmental Inspectors conducted onsite environmental training as needed.
- Began installing various signage around Project sites.
- Began site preparation and equipment mobilization of the 69th Street Staging Yard. ²

TABLE 1-1 Williston-Tioga-Minot Reroute ¹			
Work Completed during Reporting Period			
<ul style="list-style-type: none"> • Mobilization of construction material and equipment. ² • Contacted North Dakota One Call to survey for buried utility lines within the construction ROW. ² • Completed clearing / grading of construction ROW. • Completed ditching for pipeline reroute. 			
Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	100%	100%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	100%	100%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Hydrostatic Testing	0%	0%	
Work Planned for next Reporting Period and Schedule Changes:			
<ul style="list-style-type: none"> • Begin stringing, welding and coating of pipeline for the reroute. 			
Problem Areas, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> • No problem areas were identified during reporting period. 			
Non-Compliance Issues, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> • No non-compliance issues were identified during reporting period. 			

¹ This reroute was included as part of WBI Energy's response to Environmental Condition 5 of its June 8, 2021 Response to Environmental Conditions of Order Issuing Certificate (Attachment 5-1, Table 5A, Modification Reference ID AF-1).

² These activities began on July 9, 2021.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable.

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-2
Line Section 30 Loop**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 2	0 of 2	
Bores	0 of 8	0 of 8	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Begin staking the construction ROW and potholing utility crossings.
- Begin clearing / grading activities.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.
- Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action



View of No Access sign installed at 66th Avenue along the Line Section 30 Loop.



View of resource signs installed at waterbody s-wm-ea-002 along the Line Section 30 Loop.

TABLE 1-3a
Tioga-Elkhorn Creek Pipeline- Spread 1 (MP 0.0 to 23.0)

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 2	0 of 2	
Block Valves	0 of 1	0 of 1	
Bores	0 of 4	0 of 4	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Mobilization of mowing contractor to construction ROW.
- Begin to mow the construction ROW.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-3b
Tioga-Elkhorn Creek Pipeline- Spread 2 (MP 23.0 to 62.8)**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 1	0 of 1	
Block Valves	0 of 3	0 of 3	
Bores	0 of 51	0 of 51	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-4a
Lake Sakakawea HDD
North Side of Lake Sakakawea**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Site Prep	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Pilot Hole Drilling	0%	0%	
Reaming Operations	0%	0%	
Pipe Installation	0%	0%	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Begin initial site preparation work.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-4b
Lake Sakakawea HDD
South Side of Lake Sakakawea**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Site Prep	0%	0%	
Pilot Hole Drilling	0%	0%	
Reaming Operations	0%	0%	
Swab Pass	0%	0%	
Pull Back & Pipe Installation	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Begin initial site preparation work.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-5
Tioga Compressor Lateral**

Work Completed during Reporting Period

- Began clearing / grading activities.
- Began potholing to locate existing utility lines.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	1%	1%	Installed erosion control devices.
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 2	0 of 2	
Bores	0 of 1	0 of 1	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Continue clearing / grading activities.
- Set timber mats to cross a foreign pipeline in a barrow ditch.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.
- Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-6
Elkhorn Creek to Northern Border Interconnect Pipeline**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Block Valves	0 of 1	0 of 1	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-7
Line Section 25 Loop**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 2	0 of 2	
Block Valves	0 of 2	0 of 2	
Bores	0 of 27	0 of 27	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 1-8
Uprates to Line Section 25**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	0%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Cleanup	0%	0%	
Seeding	0%	0%	
Pig Launcher/Receiver	0 of 3	0 of 3	
Bores	0 of 4	0 of 4	
Hydrostatic Testing	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable


Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

C. Construction Status – Aboveground Facilities

TABLE 2-1 Tioga Compressor Station				
Work Completed during Reporting Period				
<ul style="list-style-type: none"> • Mobilization of construction material and equipment.³ • Removed north and east side security fences for construction purposes.³ • Began initial site preparation work.³ • Continued site preparation. • Began installing erosion control devices. 				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Initial Site Work	80%	80%		
Waste Systems	0%	0%		
Foundations & Concrete	0%	0%		
Installation of Buildings	0%	0%		
Installation of Piping	0%	0%		
Installation of Structural Supports	0%	0%		
Setting of Equipment	0%	0%		
Insulation	0%	0%		
Start-Up & Commissioning - Mechanical	0%	0%		
Start-Up & Commissioning - Electrical	0%	0%		
Cleanup / Restoration	0%	0%		
Work Planned for next Reporting Period and Schedule Changes:				
<ul style="list-style-type: none"> • Complete site preparation. • Begin foundation work. 				
Problem Areas, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> • No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> • No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:				
<ul style="list-style-type: none"> • No non-compliance issues were identified during reporting period. Copies included: Not applicable				
Landowner Issues:				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

³ These activities began on July 9, 2021.

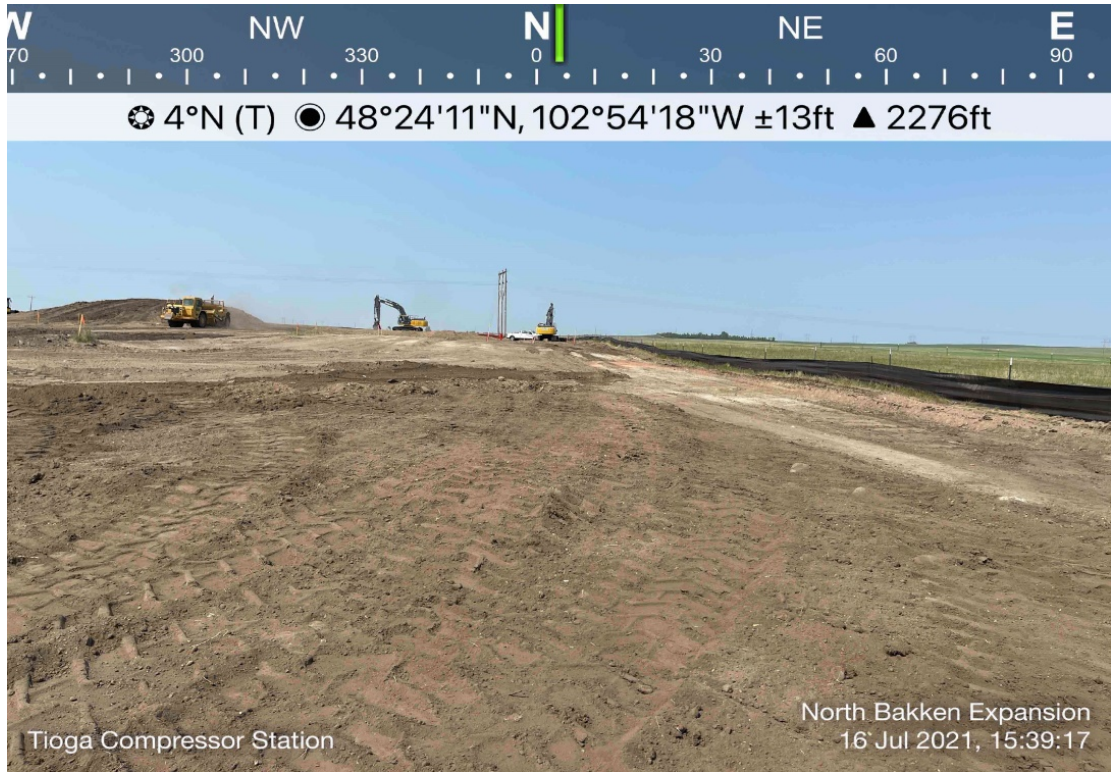

View of silt fence installed and grading activity at the Tioga Compressor Station.

**TABLE 2-2
Elkhorn Creek Compressor Station**

Work Completed during Reporting Period

- Mobilization of construction material and equipment. ⁴
- Began initial site preparation work. ⁴
- Continued site work.
- Began permanent access road construction after FERC approval of variance request V20 on July 15, 2021.
- Began installing erosion control devices.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Initial Site Work	80%	80%	Included stockpiling topsoil, installation of erosion control devices, stripping and bringing construction pad to rough grade.
Waste Systems	0%	0%	
Foundations & Concrete	0%	0%	
Installation of Buildings	0%	0%	
Installation of Piping	0%	0%	
Installation of Structural Supports	0%	0%	
Setting of Equipment	0%	0%	
Insulation	0%	0%	
Start-Up & Commissioning - Mechanical	0%	0%	
Start-Up & Commissioning - Electrical	0%	0%	
Cleanup / Restoration	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Complete construction pad and begin excavation for new buildings.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

⁴ These activities began on July 9, 2021.



View of Access Road sign installed at the Elkhorn Creek Compressor Station.



View of cut and fill activities at the Elkhorn Creek Compressor Station.



View of grading activity at the Elkhorn Creek Compressor Station.

**TABLE 3-1
Lignite Plant Receipt and Town Border Stations**

Work Completed during Reporting Period				
<ul style="list-style-type: none"> No work was completed during this reporting period. 				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Site Preparation	0%	0%		
Facility Installation	0%	0%		
Cleanup	0%	0%		
Work Planned for next Reporting Period and Schedule Changes:				
<ul style="list-style-type: none"> No work is planned for the next reporting period. 				
Problem Areas, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable				
Landowner Issues:				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 3-2
Norse Plant Receipt Station**

Work Completed during Reporting Period			
<ul style="list-style-type: none"> No work was completed during this reporting period. 			
Activity	Total % Completed This Period	% of Total Job Completed	Comments
Site Preparation	0%	0%	
Facility Installation	0%	0%	
Cleanup	0%	0%	
Work Planned for next Reporting Period and Schedule Changes:			
<ul style="list-style-type: none"> No work is planned for the next reporting period. 			
Problem Areas, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 			
Non-Compliance Issues, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 			
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:			
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable			

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

TABLE 3-3 Norse Transfer Station				
Work Completed during Reporting Period				
<ul style="list-style-type: none"> No work was completed during this reporting period. 				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Site Preparation	0%	0%		
Facility Installation	0%	0%		
Cleanup	0%	0%		
Work Planned for next Reporting Period and Schedule Changes:				
<ul style="list-style-type: none"> Power company will begin to install utility services. 				
Problem Areas, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable				
Landowner Issues:				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

TABLE 3-4 Northern Border Interconnect			
Work Completed during Reporting Period			
<ul style="list-style-type: none"> No work was completed during this reporting period. 			
Activity	Total % Completed This Period	% of Total Job Completed	Comments
Site Preparation	0%	0%	
Facility Installation	0%	0%	
Cleanup	0%	0%	
Work Planned for next Reporting Period and Schedule Changes:			
<ul style="list-style-type: none"> Begin site preparation and access road construction. 			
Problem Areas, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 			

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 3-5
Robinson Lake Plant Receipt Station**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Site Preparation	0%	0%	
Facility Installation	0%	0%	
Cleanup	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- Power company will upgrade utility services.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues:

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**TABLE 3-6
Springbrook Plant Receipt Station**

Work Completed during Reporting Period

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Site Preparation	0%	0%	
Facility Installation	0%	0%	
Cleanup	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:				
<ul style="list-style-type: none"> No work is planned for the next reporting period. 				
Problem Areas, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable				
Landowner Issues:				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

TABLE 3-7 Tioga Plant Receipt Station			
Work Completed during Reporting Period			
<ul style="list-style-type: none"> No work was completed during this reporting period. 			
Activity	Total % Completed This Period	% of Total Job Completed	Comments
Site Preparation	0%	0%	
Facility Installation	0%	0%	
Cleanup	0%	0%	
Work Planned for next Reporting Period and Schedule Changes:			
<ul style="list-style-type: none"> No work is planned for the next reporting period. 			
Problem Areas, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 			
Non-Compliance Issues, Corrective Actions and Effectiveness:			
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 			
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Response:			
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable			
Landowner Issues:			
Date	Name	Milepost / Alignment Sheet #	Problem/Concern

**TABLE 4
Changes to Stream Crossings or
Work in Environmental Sensitive Areas**

Schedule changes to stream crossings.

- No changes to stream crossings occurred during this reporting period.

Schedule changes for work in other environmentally sensitive areas.

- No changes to environmentally sensitive areas occurred during this reporting period.

Waterbodies Crossed

Approx. Milepost	Feature ID	Waterbody Name	Crossing Method
Tioga to Elkhorn Creek			
0.8	s-wm-ea-001p	Unnamed tributary to Paulson Creek	Open Cut
2.4	s-wm-ea-002	Unnamed tributary to Dry Fork Creek	Open Cut
12.3	s-wm-ee-001	Unnamed tributary to Beaver Creek	Open Cut
18.2	s-wm-eb-002	Beaver Creek	GuidedBore
24.4	s-wm-eb-003p	Lake Sakakawea	HDD
25.7	o-mk-ee-001	NaturalPond	HDD
27.1	s-mk-eb-001	Unnamed tributary to Sand Creek	Open Cut
27.5	s-mk-ea-001	Unnamed tributary to Sand Creek	GuidedBore
29.0	s-mk-wa-001	Unnamed tributary to Tobacco Garden Creek	GuidedBore
30.3	s-mk-eb-002	Tobacco Garden Creek	GuidedBore
36.5	s-mk-ea-003	Tobacco Garden Creek	GuidedBore
39.2	s-mk-ea-002	Unnamed tributary to Tobacco Garden Creek	Open Cut
44.9	DSK_NHD_11	Timber Prong Creek	GuidedBore
44.9	DSK_NHD_5	Timber Prong Creek	GuidedBore
51.5	s-mk-eb-005	Northfork Creek	GuidedBore
52.4	s-lbt-001a	CherryCreek	GuidedBore
58.0	DSK_NHD_2	Unnamed tributary to Sevenmile Creek	Open Cut
Line Section 25 Loop			
13.4	s-bk-eb-001p	White Earth Creek	GuidedBore
Line Section 30 Loop			
7.2	s-wm-ea-002	Unnamed tributary to Dry Fork Creek	Open Cut
8.8	s-wm-ea-001p	Unnamed tributary to Paulson Creek	Open Cut
Tioga Compressor Station			
NA	o-wm-eb-001	Man-made pond	N/A
Yards			
EngetYard	o-mt-ee-001	Man-made pond	N/A

Wetlands Crossed or Otherwise Affected by Project

Approx. Milepost	Feature ID	Crossing Method
Tioga to Elkhorn Creek		
0.9	w-wm-ea-008e	Open Cut
12.8	w-wm-ee-001e	Open Cut
16.9	w-wm-eg-001e	Open Cut
18.0	w-wm-eb-008e	Open Cut
28.0	w-mk-ea-001e	Open Cut
29.3	w-mk-eb-002e	Open Cut
38.5	w-mk-ea-003e	Guided Bore
40.0	w-mk-ef-004e	Open Cut
41.5	w-mk-eb-003e	Open Cut
44.9	DSK_NWI_7	Guided Bore
47.0	w-mk-ea-004e	Guided Bore

51.0	w-mk-eb-004e	Open Cut
52.5	w-lbt-003	Open Cut
52.6	w-lbt-001b	Open Cut
52.6	w-lbt-001a	Open Cut
53.7	w-mk-wa-002e	Open Cut
55.0	w-mk-ef-007e	Open Cut
55.0	w-mk-wa-001e	Open Cut
55.7	w-mk-ef-008e	Open Cut
62.4	w-mk-eg-001	Open Cut
Line Section 25 Loop		
0.7	w-wm-eb-002e	Guided Bore
4.7	w-wm-ea-002e	Open Cut
4.8	w-wm-ea-001e	Open Cut
9.8	w-mt-ea-001e	Open Cut
11.0	w-bk-ea-013	Open Cut
11.9	w-bk-ea-005e	Open Cut
11.9	w-bk-ea-006e	Open Cut
13.2	w-bk-ee-002e	Open Cut
13.5	w-bk-eb-001e	Guided Bore
14.8	w-bk-wa-001e	Guided Bore
16.0	w-bk-ea-003e	Open Cut
16.1	w-bk-ea-002e	Open Cut
16.3	w-bk-ea-001e	Guided Bore
Line Section 30 Loop		
0.0	w-wm-ee-002e	Open Cut
0.2	w-wm-ec-004e	Open Cut
0.3	w-wm-ec-005e	Open Cut
0.4	w-wm-ef-002e	Open Cut
5.8	w-wm-ec-003e	Open Cut
8.7	w-wm-ea-008e ^c	Open Cut
Uprating Existing Line		
N/A	w-bk-ea-010e	Guided Bore
Access Roads		
N/A	w-wm-eb-009e	N/A - Matting
Yards		
N/A	w-wm-ef-004e	N/A - Matting
N/A	w-wm-ef-005e	N/A - Matting
