



---

1250 West Century Avenue  
Mailing Address:  
P.O. Box 5601  
Bismarck, ND 58506-5601  
(701) 530-1600

August 15, 2024

Debbie-Anne Reese, Acting Secretary  
Federal Energy Regulatory Commission  
888 First Street, N.E., Room 1A  
Washington, D.C. 20426

Re: WBI Energy Transmission, Inc.  
Wahpeton Expansion Project  
Docket No. CP22-466-000  
Weekly Status Report No. 37

Dear Acting Secretary Reese:

WBI Energy Transmission, Inc. (WBI Energy) herewith submits its Weekly Status Report No. 37 for the Wahpeton Expansion Project, in compliance with Environmental Condition 9 of the Appendix to the Federal Energy Regulatory Commission's October 23, 2023 Order Issuing Certificate in the above referenced docket.

The attached report addresses the status of the project from August 05, 2024 to August 11, 2024.

Should you have any questions or comments regarding this filing, please call the undersigned at (701) 530-1563.

Sincerely,

/s/ Lori Myerchin

Lori Myerchin  
Vice President, Regulatory Affairs  
and Transportation Services

Attachment

cc: via email  
David Hanobic, FERC Environmental Project Manager  
Dawn Ramsey, FERC  
Official Service List



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 37  
 Reporting Period: 8-05-2024 – 8-11-2024

**A. Update on Federal Authorizations**

- WBI Energy has obtained all necessary federal permits and authorizations required for construction of the Wahpeton Expansion Project.

**B. Construction Status – Pipeline Facilities**

- Environmental Inspectors continue to conduct onsite environmental training as needed.
- On August 9, 2024, FERC approved a variance request to modify procedures in the *Plan for Unanticipated Discovery of Historic Properties or Human Remains During Construction* for the discovery of additional cultural materials at a historic artifact scatter site.

**TABLE 1-1**  
**Wahpeton Expansion Pipeline**

**Work Completed during Reporting Period:**

- Continued surveying and staking the construction right-of-way and approved access roads.
- Continued clearing/grading, stringing, welding, joint coating, ditching, lowering, and backfill activities.
- Completed boring activities at six bores and continued boring activities at other bore sites.
- Continued construction activities at Valve Site Nos. 2, 4 and 5.
- Continued installation and maintenance of Project signage, equipment mats, erosion control devices, and goal posts at aboveground utility lines.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
<b>Pipeline</b>			
Clearing / Grading	8%	92%	
Stringing	12%	87%	
Bending	0%	78%	
Welding	10%	70%	
Joint Coating	14%	54%	
Ditching	5%	39%	
Lowering	4%	38%	
Backfill	4%	32%	
Bores	6 of 68	38 of 68	Completed Bores 33, 36, 37, 38, 40 and 46.
Cleanup	0%	8%	
Seeding	0%	0%	
Final Tie-in and Commissioning	0%	0%	
Hydrostatic Testing	0 of 2	0 of 2	
<b>Appurtenant Facilities <sup>1</sup></b>			
Valve Site #1 and Pig Launcher / Receiver #1 at MP 0.0	2 of 2	2 of 2	
Cleanup/Restoration	0%	85%	

<sup>1</sup> Cleanup/Restoration includes backfilling and spreading of gravel.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 37  
 Reporting Period: 8-05-2024 – 8-11-2024

Valve Site #2 and Pig Launcher / Receiver #2 at MP 11.6	0 of 2	0 of 2	45% completion – block valve mechanically complete.
Cleanup/Restoration	0%	0%	
Valve Site #3 at MP 23.4	0 of 1	0 of 1	60% completion.
Cleanup/Restoration	0%	0%	
Valve Site #4 at MP 31.3	0 of 1	0 of 1	30% completion – continued block valve construction.
Cleanup/Restoration	0%	0%	
Valve Site #5 and Pig Launcher / Receiver #3 at MP 39.5	0 of 2	0 of 2	30% completion - continued block valve construction.
Cleanup/Restoration	0%	0%	
Valve Site #6 at MP 48.9	0 of 1	0 of 1	5% completion.
Cleanup/Restoration	0%	0%	
Valve Site #7 and Pig Launcher / Receiver #4 at MP 60.5	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	

**Work Planned for next Reporting Period and Schedule Changes:**

- Complete clearing / grading activities.
- Continue remaining pipeline construction activities.
- Continue construction activities at Valve Site Nos. 4, 5, 6, and 7.
- Continue installation and maintenance of Project signage, erosion control devices, equipment mats, and goal posts at aboveground utility lines.
- Continue surveying and staking the construction right-of-way and approved access roads.
- Begin boring activities at Bores 41, 47, 48 and 50.

**Problem Areas, Corrective Actions and Effectiveness:**

- No problem areas were identified during reporting period.

**Non-Compliance Issues, Corrective Actions and Effectiveness:**

- No non-compliance issues were identified during reporting period.

**Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:**

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

**Landowner Issues: None**

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/05/2024

Location: Sta. No. 2240+00

Notes: No construction occurred on the construction right-of-way due to a rain event.



Date: 8/05/2024

Location: Sta. No. 2636+00

Notes: Erosion control devices and goal posts on the construction right-of-way.





**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/06/2024

Location: Sta. No. 1160+50

Notes: Backfilling activities on the construction right-of-way.



Date: 8/06/2024

Location: Sta. No. 1278+00

Notes: Completed bore of the  
Sheyenne River (scab006p) (Bore  
32).





Date: 8/06/2024

Location: Sta. No. 2100+00

Notes: Completed equipment bridge and erosion control devices at a waterbody (sria002e) along the construction right-of-way.



Date: 8/06/2024

Location: Sta. No. 2175+00

Notes: Welding activities on the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/06/2024

Location: Sta. No. 3019+00

Notes: Clearing activities on the construction right-of-way.



Date: 8/07/2024

Location: Sta. No. 268+40

Notes: Hydrostatic testing of bore pipes (Combined Bores 7 and 8).



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/07/2024

Location: Sta. No. 2551+00

Notes: No construction occurred on the construction right-of-way due to a rain event.



Date: 8/08/2024

Location: Sta. No. 550+00

Notes: Tie-in of bore pipe at Bore 18 along the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/09/2024

Location: Sta. No. 665+00

Notes: Tie-in of bore pipe at Bore 21 along the construction right-of-way.



Date: 8/09/2024

Location: Sta. No. 2370+00

Notes: Installed equipment bridge over Pitcairn Creek (srid002p) and erosion control devices along the construction right-of-way.

**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/09/2024

Location: Sta. No. 2969+00

Notes: Pipe unloading activities on the construction right-of-way.



Date: 8/10/2024

Location: Sta. No. 777+00

Notes: Continued maintenance of erosion control devices and signage at a wetland (wcae006e) along the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024



Date: 8/10/2024

Location: Sta. No. 1267+00

Notes: Backfilling activities along the construction right-of-way.




Date: 8/10/2024

Location: Sta. No. 1771+665

Notes: Installed secondary containment for boring equipment for a guided bore (Bore 41) on the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 37  
Reporting Period: 8-05-2024 – 8-11-2024

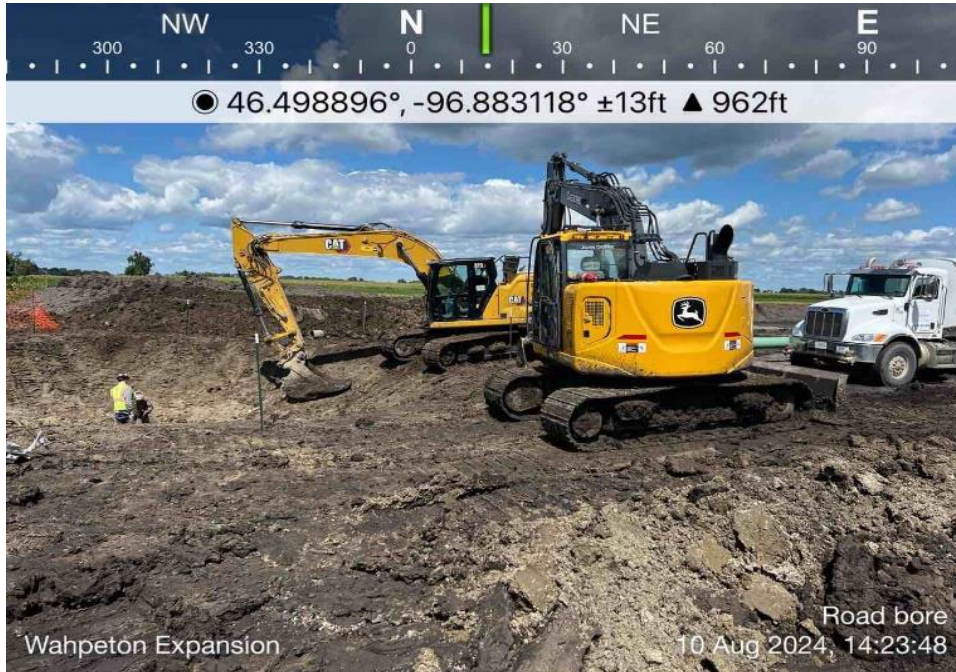

Date: 8/10/2024

Location: Sta. No. 1980+00

Notes: Boring activities at Bore 46.





**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 37  
 Reporting Period: 8-05-2024 – 8-11-2024

**C. Construction Status – Aboveground Facilities**

TABLE 2-1

Modifications at Mapleton Compressor Station

Work Completed during Reporting Period:

No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Install Aboveground Station Piping	0%	0%	
Install Belowground Station Piping	0%	0%	
Cleanup / Restoration <sup>2</sup>	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:

No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues: None

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

<sup>2</sup> Final cleanup and restoration will be in conjunction with Block Valve #1 and Pig Launcher / Receiver #1 within the compressor station yard.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 37  
 Reporting Period: 8-05-2024 – 8-11-2024

**TABLE 2-2**  
**MDU- Kindred Border Station**

**Work Completed during Reporting Period:**

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Initial Site Work	0%	38%	
Concrete Work	0%	0%	
Install Aboveground Piping	0%	0%	
Install Belowground Piping	0%	0%	
Install Buildings	0%	0%	
Cleanup / Restoration <sup>3</sup>	0%	0%	
Install Security Fence	0%	0%	

**Work Planned for next Reporting Period and Schedule Changes:**

- No work is planned for the next reporting period.

**Problem Areas, Corrective Actions and Effectiveness:**

- No problem areas were identified during reporting period.

**Non-Compliance Issues, Corrective Actions and Effectiveness:**

- No non-compliance issues were identified during reporting period.

**Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:**

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

**Landowner Issues: None**

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

<sup>3</sup> Final cleanup and restoration will be completed in conjunction with Block Valve #3 within the border station yard.





**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 37  
 Reporting Period: 8-05-2024 – 8-11-2024

**TABLE 2-3**  
**MDU- Wahpeton Border Station**

**Work Completed during Reporting Period:**

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Initial Site Work	0%	0%	
Concrete Work	0%	0%	
Install Aboveground Piping	0%	0%	
Install Belowground Piping	0%	0%	
Install Buildings	0%	0%	
Cleanup / Restoration <sup>4</sup>	0%	0%	
Install Security Fence	0%	0%	

**Work Planned for next Reporting Period and Schedule Changes:**

- Begin initial site work.

**Problem Areas, Corrective Actions and Effectiveness:**

- No problem areas were identified during reporting period.

**Non-Compliance Issues, Corrective Actions and Effectiveness:**

- No non-compliance issues were identified during reporting period.

**Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:**

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

**Landowner Issues: None**

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**D. Changes to Stream Crossings or Work in Environmental Sensitive Areas**

**TABLE 3**  
**Changes to Stream Crossings or**  
**Work in Environmental Sensitive Areas**

**Schedule changes to stream crossings.**

- None during reporting period.

**Schedule changes for work in other environmentally sensitive areas.**

- None during reporting period.

<sup>4</sup> Final cleanup and restoration will be completed in conjunction with Block Valve #7 and Pig Launcher / Receiver #4 within the border station yard.
